Lab 2 Submission

Agile Backlog Creation & Sprint Simulation in Jira

Problem Statement #54 — Local Sports Tournament & Bracket Manager

---

Jira Project / Workspace Link:
https://kshitijprabhu06.atlassian.net/jira/software/projects/TBM/boards
Jira key: TBM
Two sprints completed: TBM Sprint 1 and TBM Sprint 2
Kshitij Prabhu – PES1UG24CS914 – Section 5B

1. Jira Backlog — Epics, User Stories & Story Points

Backlog view showing TBM Sprint 1 and the general Backlog — each user story tagged with its parent Epic and Fibonacci story point estimate. Three Epics span the project: Team Registration & Bracket Setup, Live Match Scoring, and Standings & Tiebreakers.

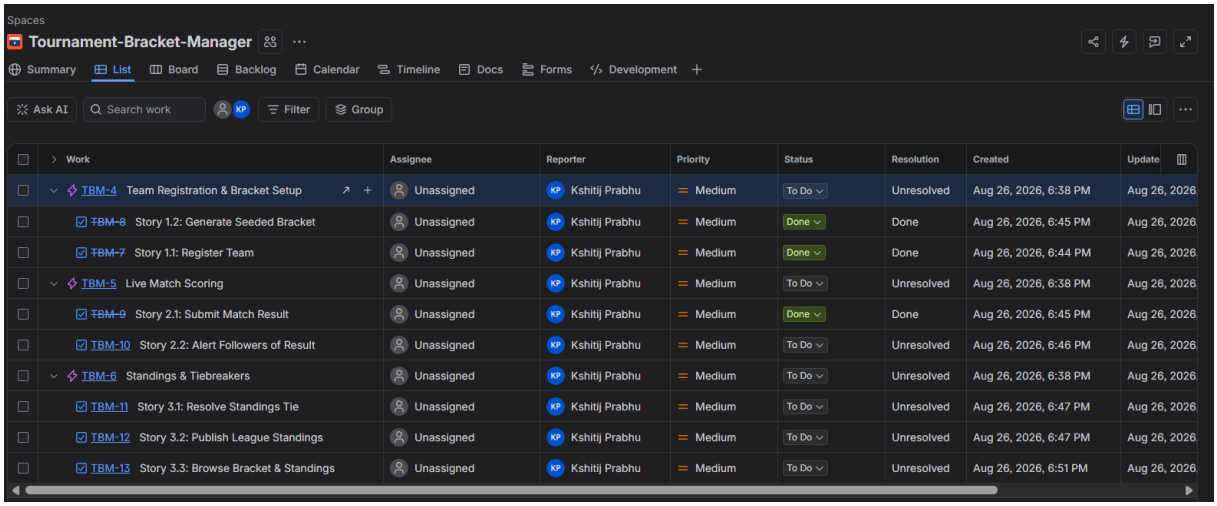


Fig. 1 — Backlog with Epics, User Stories, and story point assignments.

2. Sprint Board — Story Points

Close-up view of a user story showing its Fibonacci story point estimate assigned in Jira.

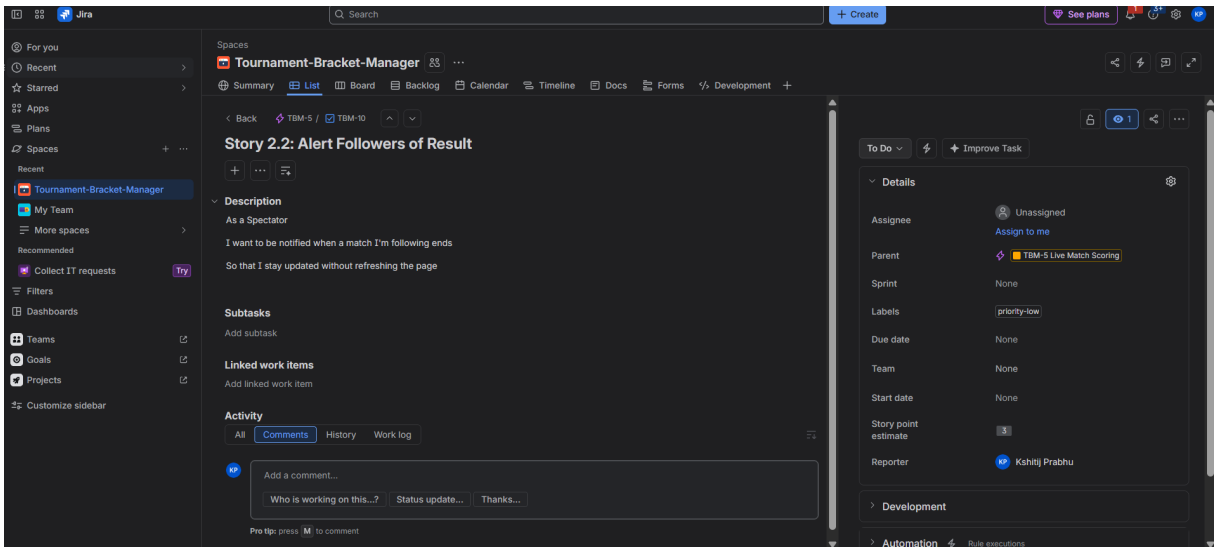


Fig. 2 — Story points assigned to a user story.

3. Active Sprint Board

Sprint board view showing stories progressing through To Do / In Progress / Done across the three Epics: Team Registration & Bracket Setup, Live Match Scoring, and Standings & Tiebreakers.

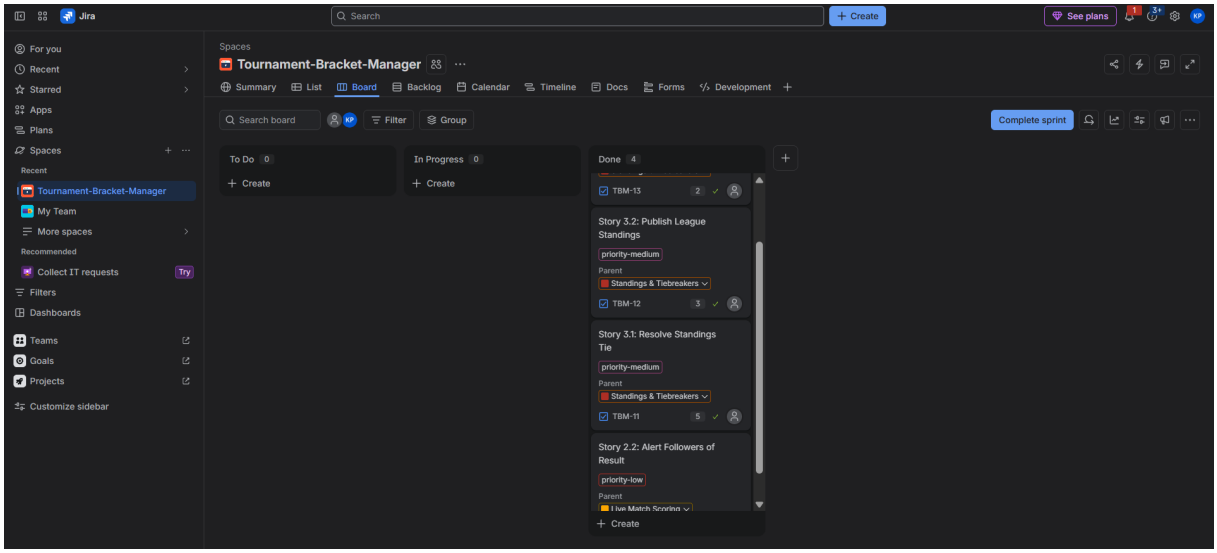


Fig. 3 — Active sprint board view.

4. Burndown Chart

Burndown chart tracking remaining story points against the ideal guideline burn rate over the sprint window. Remaining work dropped as stories were moved to Done across both sprints.



Fig. 4 — Sprint burndown chart (Story Points vs. time).

5. Reflection Questions

Did the story point estimations reflect the actual effort required?

Mostly yes. Generate Seeded Bracket (8 points) was the most complex story to size — it depends on registration being finalized first and has to handle both single- and double-elimination formats. The smaller stories (2–3 points), like browsing standings or alerting followers of a result, were straightforward to estimate and matched their actual scope well. Stories in the middle range (5 points) such as Register Team and Submit Match Result felt correctly placed — they each have one well-scoped interaction surface but require validation and state changes downstream.

Was the backlog well-prioritized?

Yes. Register Team, Generate Seeded Bracket, and Submit Match Result were all marked High priority because every other story in the backlog depends on them — you cannot score a match or publish standings before teams are registered and a bracket exists. Notifications and browsing standings were Low priority since they are helpful but not required to run the tournament. Epic 1 (Team Registration & Bracket Setup) was scheduled first to establish the foundation; Epic 3 (Standings & Tiebreakers) was left for Sprint 2 since it only becomes meaningful once matches are being played.

How did the simulated sprint align with the original plan?

Sprint 1 covered the critical path: Register Team (TBM-2), Generate Seeded Bracket (TBM-3), and Submit Match Result (TBM-5) — the three stories that must exist before anything else can run. Sprint 2 built on top of that foundation with Resolve Standings Tie (TBM-6), Publish League Standings (TBM-7), Alert Followers of Result (TBM-4), and Browse Bracket & Standings (TBM-8). Splitting this way meant Sprint 1 delivered a working core loop and Sprint 2 layered in the visibility and notification features that depend on it.

What insights did the burndown chart give about team capacity?

The burndown chart shows remaining story points dropping as stories were moved to Done across the sprint. Since this was a simulated solo sprint rather than a real multi-person team tracking hours day by day, the burn pattern reflects batch transitions rather than a gradual daily staircase. The more useful signal is the split between Sprint 1 (18 points: 3 high-priority stories) and Sprint 2 (13

points: 4 lower-priority stories) — this distribution suggests a realistic per-sprint capacity of around 13–18 points for a solo developer, with the higher-complexity stories (bracket generation, match scoring) absorbing most of the effort in Sprint 1.

End of submission — Lab 2: Agile Backlog Creation & Sprint Simulation in Jira.
